

**CHOLERA RESPONSE UPDATES  
KAKUMA REFUGEE CAMP/KALOBYEI SETTLEMENT  
01/06/2017**




**Update No. 1**

**1. Highlights**




- Cholerae outbreak ongoing with the first confirmed case identified on 22<sup>nd</sup> May 2017.
- A total of 3 samples already confirmed for Vibrio Cholerae inaba 01
- 58 Patients currently lined up. 38 in Kakuma and 20 in Kalobeyi.
- 2 CTCs operational with
  - a) Kalobeyi CTC - 7 patients currently admitted.
  - b) Kakuma 4 CTC - 2 patients currently admitted
- No mortality reported to date.

**STATISTICS**

**KAKUMA REFUGEE CAMP**

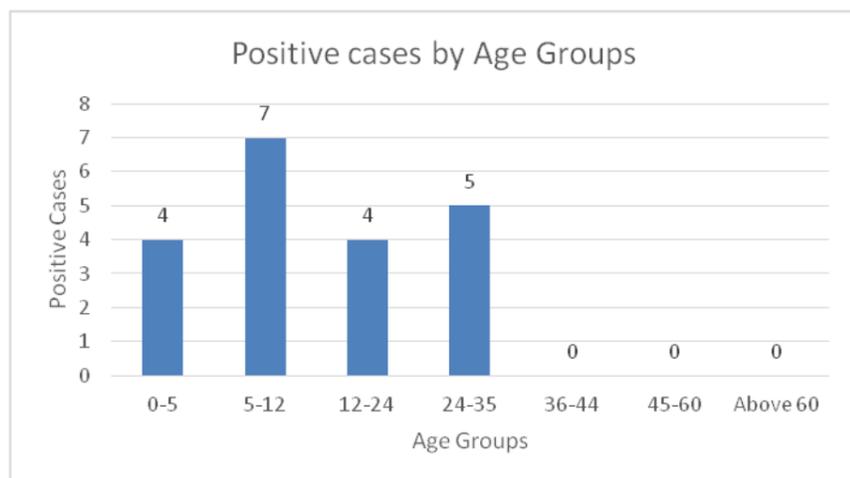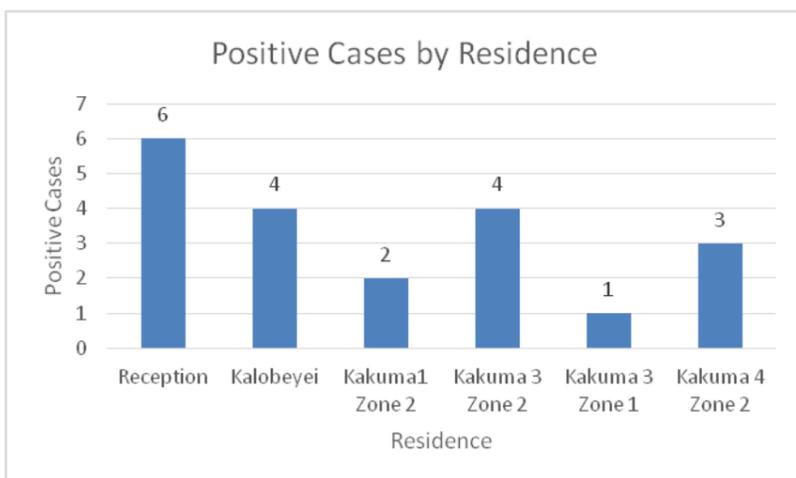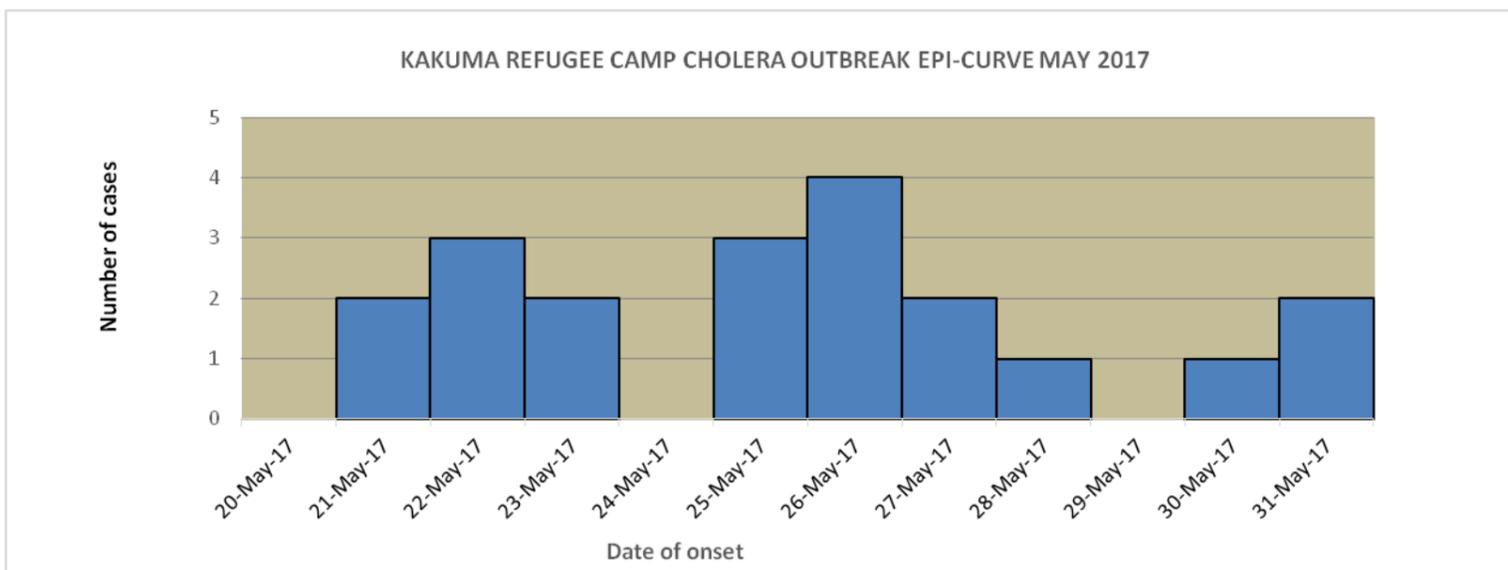

## KALOBYEI SETTLEMENT

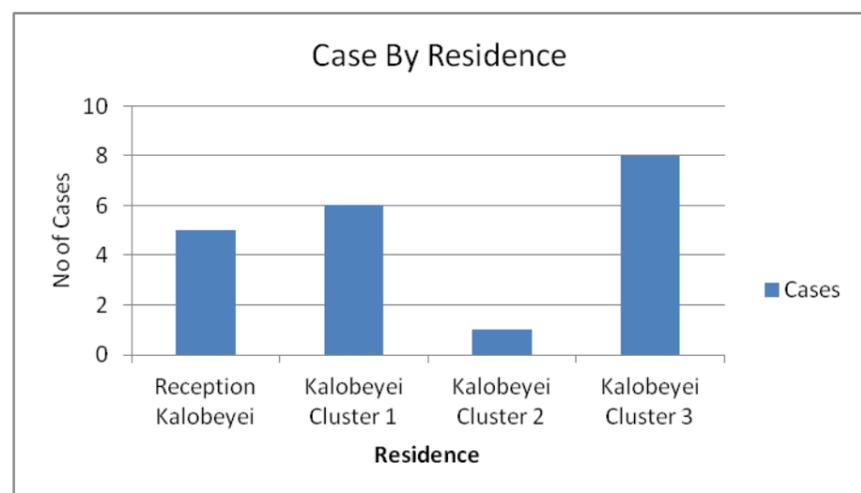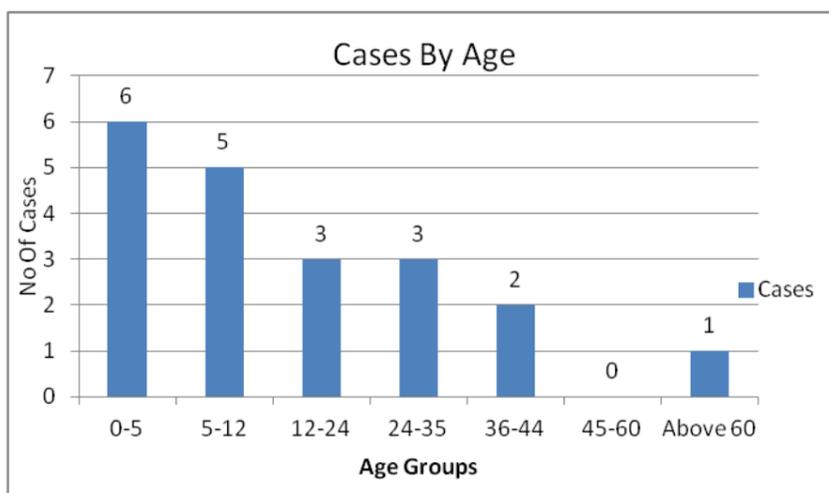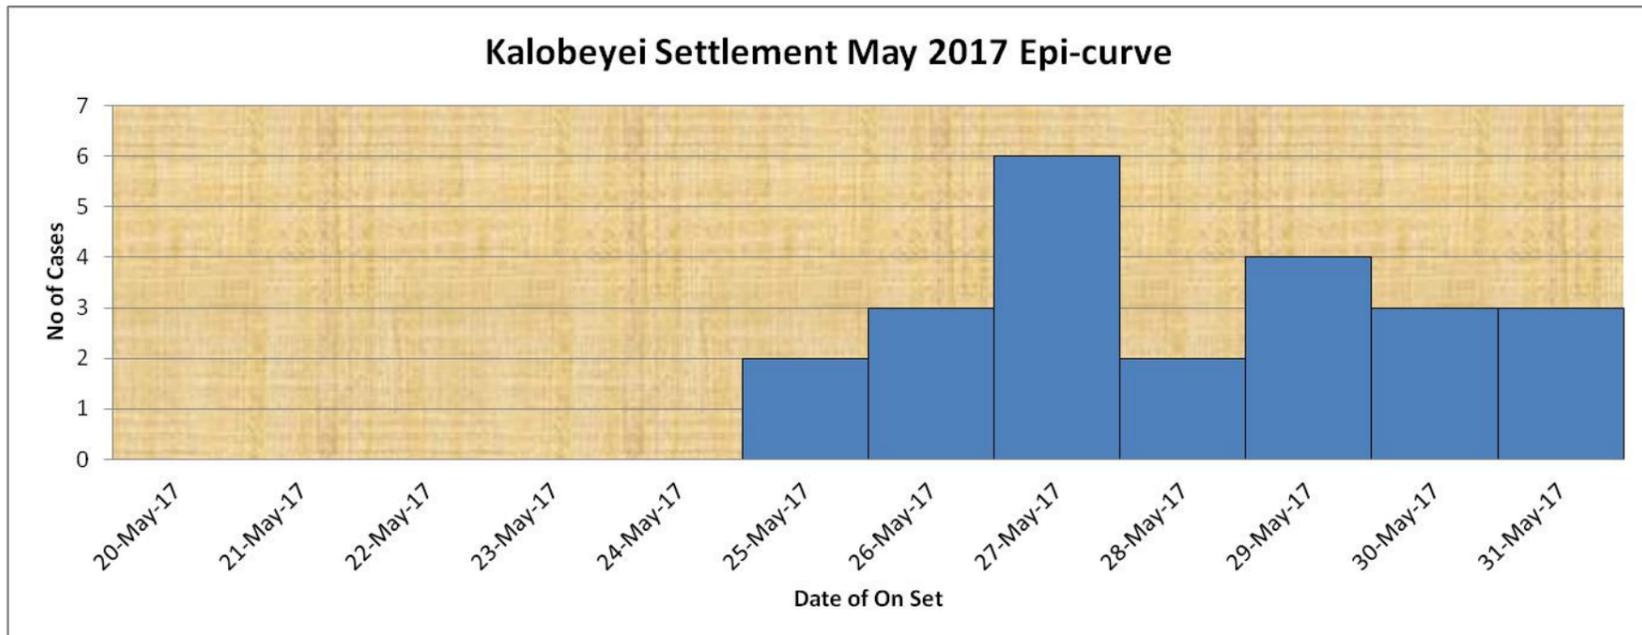

### 1. Water, Sanitation and Hygiene

#### Water

NRC is the main WASH implementing partner In Kakuma and Kalobeyei. Other operational WASH partners are Team & Team and World Vision International-Kenya.

#### Kakuma

Average water supply in Kakuma is 21litres pppd

- Extra pipeline done in Kakuma 1 Zone 2 increase water supply to tap stands. Currently 4 of the 5 tap stands in the zone are currently working.
- Repair of all broken taps and nozzles ongoing in Kakuma 1 Zone 2, Kakuma 3 and Kakuma 4.
- Connection of CTC in Kakuma 4 with a direct line completed to ensure continuous running water.
- Repair of pumping system in borehole 15 complete increasing availability of water in Kakuma.
- An additional elevated steel tank in kakuma 1 connected to bore hole 3 and ready for use.
- Water distribution timetable changed in Kakuma 4 aimed at making water more accessible. Close monitoring with household surveys to establish effectiveness of change

#### Kalobeyei

- Population in Kalobeyei currently receiving 12 litres pppd.
- Kalobeyei divided into three Clusters. Cluster 1 currently connected piped water while cluster 2 & 3 rely on trucked water from Cluster 1.
- An extra elevated still tank connected to water in Cluster on that will ensure the reception centre in kalobeyei has continuous supply of piped water.
- Connection of T-joints done in cluster 3 from the main pipe with the same anticipated to start in cluster 2.
- 4" inch pipes mobilised in cluster 3 to connect the households to piped water from the main pipe.

- Excavation of 2,542 meters done to lay pipeline in cluster 2&3 so as to provide piped water.

## **Sanitation**

### **Kalobeyei**

- 10 additional communal latrines done in Kalobeyei cluster 3.
- Joint identification with shelter team of areas where new arrivals will be settled done so as to put sanitation facilities.

### **Kakuma**

- Two house hold latrines done for contacts of cholera patients who had sold previous latrine materials.
- Decontamination done in kakuma 3&4 of latrines of contacts admitted in kakuma 4 CTC last two days.

## **Hygiene Promotion**

### **Kalobeyei**

- Two hand washing facilities put up at the Kalobeyei reception centre.
- Decision to put leaky 5 litre jerrican in all latrines at the reception centre with 0.02% chlorine done as handwashing facilities.
- Disinfection of latrines and homes of contacts of cholera patients ongoing in Cluster 1,2&3.
- Increased Hygiene promotion messaging ongoing at the reception center in Kalobeyei.

### **Kakuma**

- Increased hand washing and hygiene promotion done in schools-Mogadishu schools done yesterday.
- Joint awareness by hygiene promoters and community health workers at household level ongoing especially in kakuma 1 3&4
- Temporary latrine construction ongoing in kakuma reception centre. Currently 8 additional latrines are complete.
- Construction of 12 door permanent latrines at kakuma reception centre by Team and Team ongoing.

## **Cholera Coordination**

-Cholerae interagency coordination done on 31.05.2017 with MoH from National, County and Subcounty, UNICEF, CDC, WHO with UNHCR and its Health and WASH implementing and operational partners. Meetings to be held twice a week.

-WASH coordination meeting to be held on 2<sup>nd</sup> June 2017
