



Improvement of shelter units in Domiz camp/Duhok, A. GHAZAL

- The total shelter capacity of the 10 refugee camps is 19,453 shelter units.
- 15,666 (74%) shelter units are improved (provided with concrete slab, kitchen, family latrine and shower) and occupied.
- More than 13,400 refugee households (about 67,000 persons) are benefiting from improved

JUNE HIGHLIGHTS

A total of 1,052 shelter units have been improved in first half of 2015 in KR-I.

The construction of 789 new shelter units is planned and the construction works will be started in July 2015. The remaining 2,998 shelter units will have to be constructed including site development works subject to availability of fund.

Erbil (4 camps):

Darashakran: A total of 2,172 improved shelter units are constructed out of which 1,952 shelter units are occupied and remaining 220 shelter units will be occupied once construction of WASH facilities is complete. It is expected to complete the construction of WASH facilities by September 2015.

Basirma: A total of 639 improved shelter units are constructed out of which 511 shelter units are occupied and construction of WASH facilities for remaining 128 shelter units is in progress. There is need to construct 66 improved shelters, however there is no fund available.

Kawergosk: A total of 512 improved shelters are constructed and occupied. The construction of 285 improved shelters was planned to be started in June 2015, however it is delayed by 1 month due to change in layout. There is need to construct 870 improved shelters, however there is no fund available.

Qushtapa Camp: A total of 758 improved shelters are constructed and occupied. The construction of 312 improved shelters is planned to be started in July 2015. There is need to construct 796 improved shelters, however there is no fund available.

Duhok (4 camps):


Domiz 1&2: A total of 7,392 improved shelters are constructed and occupied except 654 improved shelters. The relocation of refugees to 654 improved shelter units will take place in July 2015. The construction of 56 improved shelter units is planned to be started in July 2015.

Gawilan camp: A total of 1,850 improved shelters are constructed and 1,584 shelter units are occupied. There is space for 450 improved shelter units in transit area and there is space for additional 1,264 improved shelter units in empty land within the camp.



Akre: This is an old exist building. There are 283 families living in Akre and there is need to repair roof and other parts of the building.



\$55.45 million required in 2015
\$11.90 million received by June 2015



IRAQ RESPONSE INDICATORS: JUNE 2015

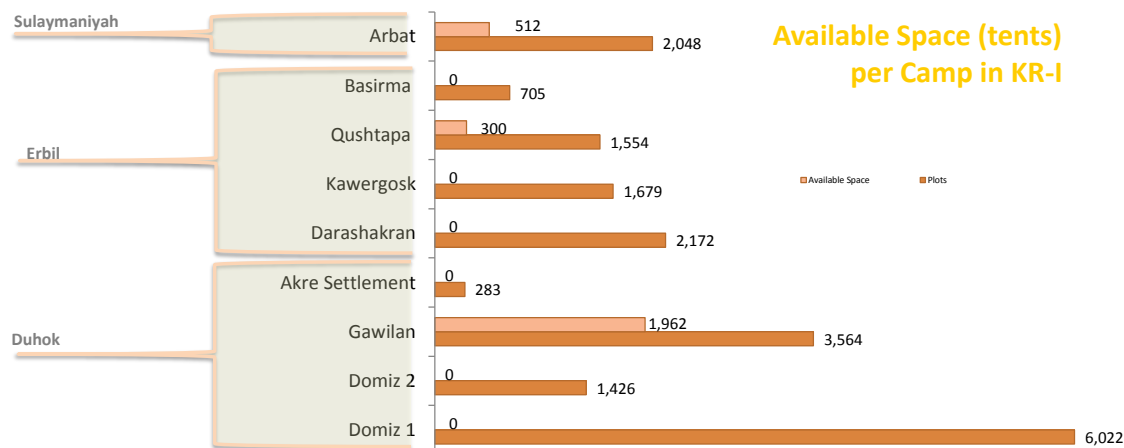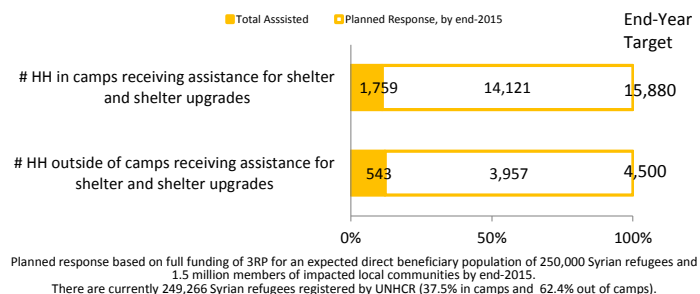

Available Space (tents) per Camp in KR-I
