



SEPTEMBER HIGHLIGHTS:

The overall situation of the sector: the total shelter capacity of 10 refugee camps is 19,999 shelter units. A total of 15,726 (80%) improved shelter units are constructed (provided with concrete slab, kitchen, family latrine and shower) and 14,831 are occupied. More than 13,800 refugee households (about 68,000 persons) are benefiting from improved shelter assistance in the camps.

A total of 1,052 new shelter units have been constructed in first half of 2015 in KR-I. The construction of an additional 1,146 new shelter units is planned out of which, the construction works for 653 shelter units have been started and construction works for remaining 493 shelter plots will be started in October 2015. A total of 2,640 shelter units is planned as part of 3RP 2016.

Erbil (4 camps):

Darashakran: A total of 2,172 improved shelter units are constructed. An additional 308 new shelter plots are planned to be constructed in October. 1,952 out of 2172 shelter units are occupied and remaining 220 shelter units will be occupied once construction of WASH facilities is complete. It is expected to complete all the construction works by end of December 2015.

Basirma: A total of 705 improved shelter units are constructed and 639 are occupied. There is need to construct 66 improved shelters, which is planned for next year. However construction of greywater channel for 76 shelter units is on hold due to land issue.

Kawergosk: A total of 524 improved shelters are constructed and occupied. The construction of 285 improved shelter units (Shelter works) has been completed by DRC. KURDs will start the construction of WASH facilities in October. Construction of 300 shelters plots are planned to be constructed in 2016 as there is not enough space available for construction of required number of shelter plots to accommodate all refugees currently living in the camp.

Qushtapa Camp: A total of 758 improved shelters are constructed and occupied. The construction of 312 improved shelters is ongoing by DRC. For the new extension (185 shelters), construction works have been postponed till October 2015 due to layout redesign. There is need to construct 484 improved shelters, which is planned in 2016.

Duhok (4 camps):

Domiz 1&2: A total of 7,392 improved shelters are constructed and occupied. The construction of 56 improved shelters is ongoing and the construction works are expected to be completed soon. In addition to that renovation of the (residency office) public buildings, police office, Public garden and construction of a distribution point have been started. Construction of 750 new shelter plots is planned in 2016.

Gawilan: A total of 1,850 improved shelters are constructed and 1,598 shelter units are occupied. There is space for 450 improved shelter units in transit area and there is space for additional 1,264 improved shelter units in empty land within the camp. In addition to this renovation of the Assyrian office, construction of distribution point and Camp Administration office has been started. Construction of 750 new shelter plots is planned in 2016.

Akre: This is an old exist building. There are 283 families living in Akre and there is need to repair roof and other parts of the building. THW is doing electrical repair, minor rehabilitation for doors and windows and construction of additional 300m² of partition walls.



Non Camp:

Sulaymaniyah: An assessment has been conducted by UNHCR and Qandil to renovate 50 houses including electrical, plumbing and WASH works. These houses were selected according to UNHCR vulnerability criteria. Qandil started the renovation works and will be completed in October 2015.



shelters improvement in Darashakran camp, Erbil. UNHCR/M. Al-nkshbandi

IRAQ RESPONSE INDICATORS: September 2015

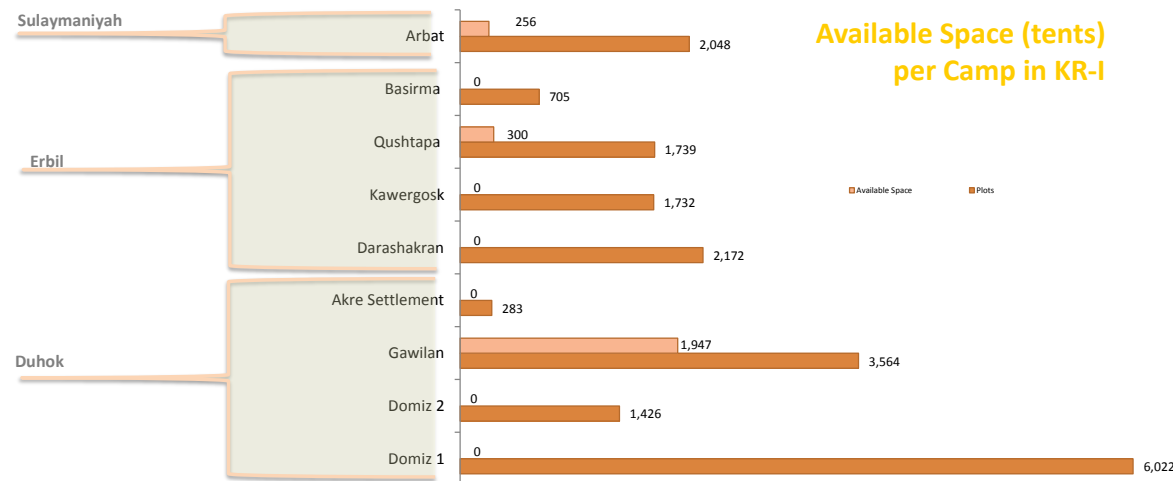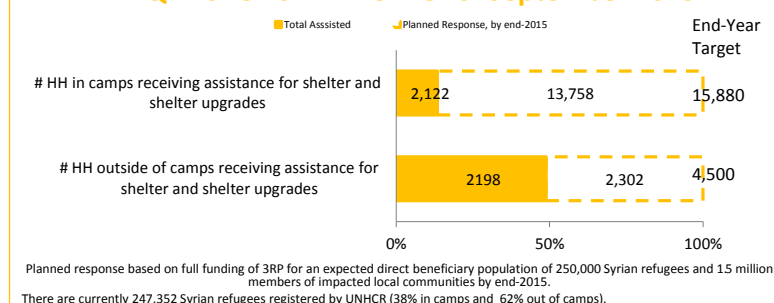

Available Space (tents) per Camp in KR-I
